

)	0	Task Mode	Task Name	Duration	Start	Finish	Predecessors
1		*	1 Design	7 days	Mon 8/28/17	Tue 9/5/17	
2		-5	1.1 Reviewing the prototypes	2 days	Mon 8/28/17	Tue 8/29/17	
3			1.2 Changes to the protoypes	1 day	Wed 8/30/17	Wed 8/30/17	2
4		-5	1.3 Review the Software Architecture	2 days	Thu 8/31/17	Fri 9/1/17	3
5		-3	1.4 Design the final Software Architecture	2 days	Mon 9/4/17	Tue 9/5/17	4
6		*	2 Development	47 days	Wed 9/6/17	Thu 11/9/17	
7	•	-5	2.1 Review the System functional specifications	4 days	Wed 9/6/17	Mon 9/11/17	5
8		-5	2.2 Review use cases	2 days	Wed 9/6/17	Thu 9/7/17	5
9		*	2.3 Coding for UI development	1 day	Fri 9/8/17	Fri 9/8/17	8
10	•	-5	2.3.1 Login/Sign Up	1 day	Fri 9/8/17	Fri 9/8/17	
11	•	-5	2.3.2 Chat	1 day	Fri 9/8/17	Fri 9/8/17	
12		-5	2.3.3 Shared Calendar	1 day	Fri 9/8/17	Fri 9/8/17	
13		-5	2.3.4 Task Management	1 day	Fri 9/8/17	Fri 9/8/17	
14		-5	2.4 Coding for server -side components	5 wks	Fri 9/8/17	Thu 10/12/17	8




	0	Task Mode	Task Name	Duration	Start	Finish	Predecessors
15		-5	2.5 UI testing	2 wks	Fri 10/13/17	Thu 10/26/17	14
16		-5	2.6 Backend testing	2 wks	Fri 10/27/17	Thu 11/9/17	15
17		-5	3 Documentation	2 days	Fri 11/10/17	Mon 11/13/17	
18		-5	3.1 Documenting the UI	2 days	Fri 11/10/17	Mon 11/13/17	16
19		-5	3.2 User Manual	1 day	Fri 11/10/17	Fri 11/10/17	16
20		-5	3.3 Installation Guide	1 day	Mon 11/13/1	Mon 11/13/17	19
21		-5	4 Testing	13 days	Tue 11/14/17	Thu 11/30/17	
22		-5	4.1 Unit Testing	5 days	Tue 11/14/17	Mon 11/20/17	20
23		-	4.2 BlackBox Testing	6 days	Tue 11/21/17	Tue 11/28/17	22
24		-	4.3 Changes after testing	2 days	Wed 11/29/17	Thu 11/30/17	23
25		-5	5 Deployment	4.25 days	Fri 12/1/17	Thu 12/7/17	
26		-5	5.1 Review the deliverables	2 days	Fri 12/1/17	Mon 12/4/17	24
27		-5	5.2 Deploy the deliverables	1 day	Tue 12/5/17	Tue 12/5/17	26
28		-9	5.3 Testing in real-time environment	1 day	Wed 12/6/17	Wed 12/6/17	27
29		-5	5.4 Final Presentation to deliver the product	2 hrs	Thu 12/7/17	Thu 12/7/17	28
30		- 5	6 Closing	4 days	Thu 12/7/17	Wed 12/13/17	




Page 2

ID	0	Task Mode	Task Name	Duration	Start	Finish	Predecessors
31		-5	6.1 Lessons Learnt Report	1 day	Thu 12/7/17	Fri 12/8/17	29
32		-5	6.2 Final changes in the project	2 days	Thu 12/7/17	Mon 12/11/17	29
33			6.3 Documenting the changes and distributing the software	2 days	Mon 12/11/17	Wed 12/13/17	32

Inactive Summary External Tasks Task Split Manual Task External Milestone Milestone Deadline **Duration-only** Project: Phoenix_GanttChart_GD Manual Summary Rollup Summary Progress Date: Tue 7/18/17 Project Summary Manual Summary Manual Progress Inactive Task Start-only Finish-only] Inactive Milestone

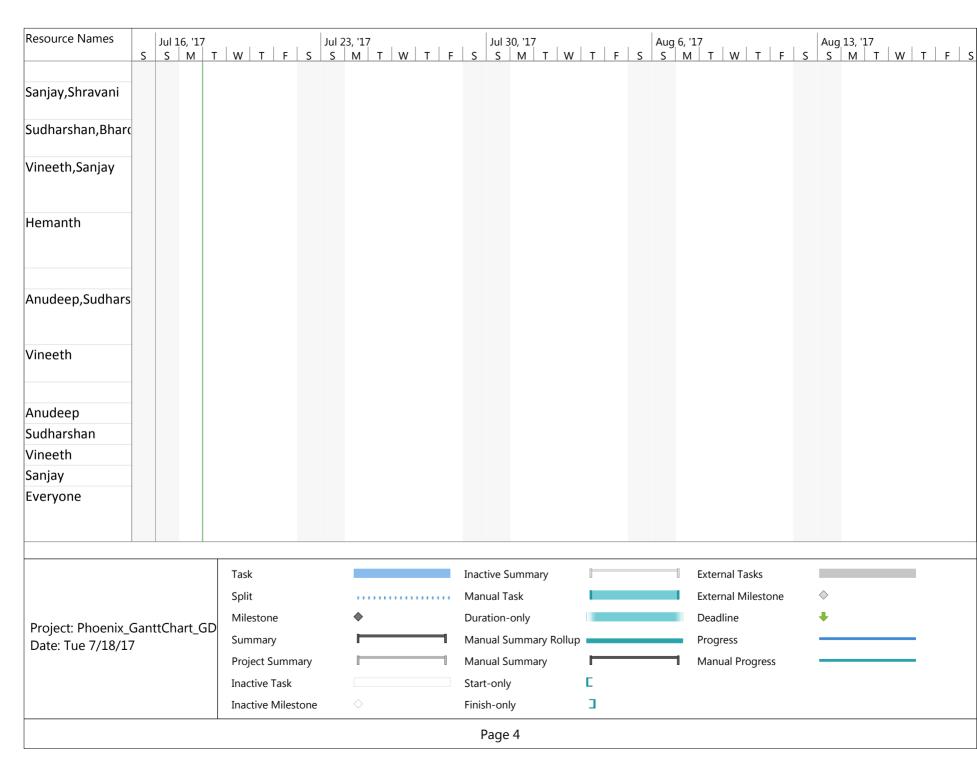

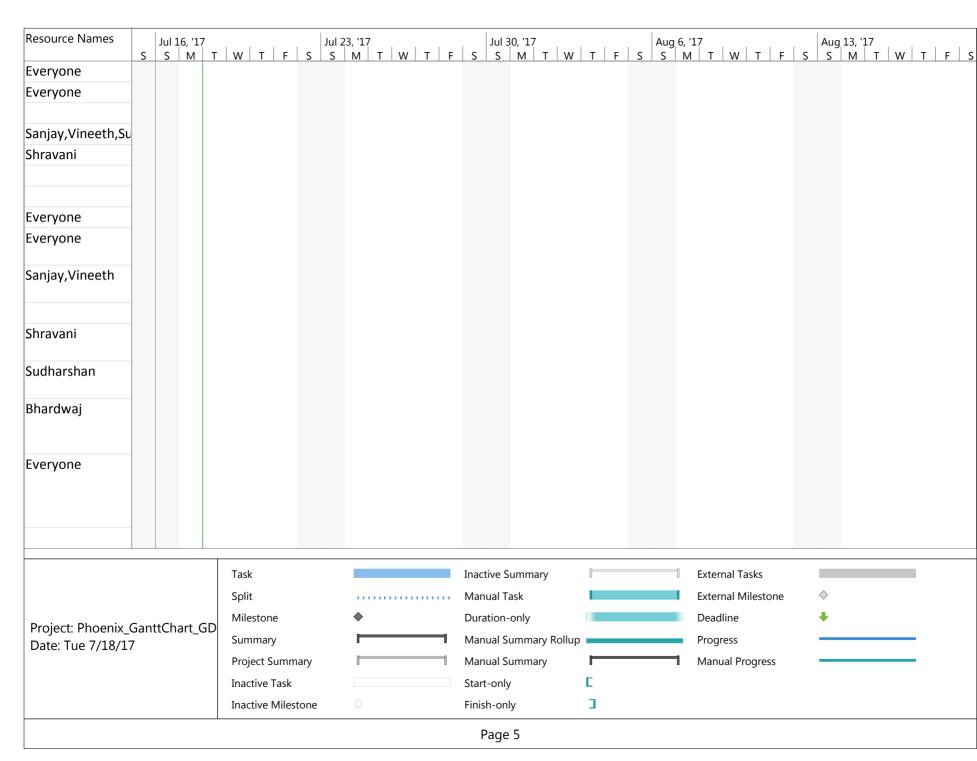

Resource Names	Jul 10, 17	_ _		. -	J, 1/	I I -	l _	Ju	I 30, '17 5 М -	_	_ _	- A	Aug 6,	'17	1 1	_ _		Aug	13, '17 M 1	_	_	_
S lemanth	Jul 16, '17 S M	T W T	F S	S S	M T	W T	F	S S	5 M -	Γ W	T F	S	S N	<u> </u>	W	T F	S	S	M 1	Γ W	T	F
Anudeep																						
Sanjay																						
,																						
		Tools						Inactive						Date	weel Tool	le.						
		Task			_				• Summary	y					rnal Tasl							
		Split						Manual	Task	y				Exte	rnal Mile			♦				
Project: Phoenix_Gant	tChart_C	Split Mileston			•			Manual Duratio	Task n-only					Exte Dea	rnal Mile dline			*				
Project: Phoenix_Gant Date: Tue 7/18/17	tChart_C	Split Mileston Summar	y		•			Manual Duratio Manual	Task n-only Summary	/ Rollup				Exte Dea Prog	rnal Mile dline Iress	estone						
Project: Phoenix_Gant Date: Tue 7/18/17	tChart_C	Split Mileston Summary Project S	y ummary	/	•			Manual Duratio Manual Manual	Task n-only Summary Summary	/ Rollup				Exte Dea Prog	rnal Mile dline	estone					-	
Project: Phoenix_Gant Date: Tue 7/18/17	tChart_C	Split Mileston Summar	y ummary Task		♦			Manual Duratio Manual	Task n-only Summary Summary	/ Rollup				Exte Dea Prog	rnal Mile dline Iress	estone						

